PROPOSED SEQUENCE OF CONSTRUCTION

GENERAL:
- SET PROJECT LIMIT BARRICADES AND SIGNING AT THE PROJECT LIMITS IN ACCORDANCE WITH THE BARRICADE AND CONSTRUCTION STANDARD SHEETS.
- COMPLETE EACH PHASE BEFORE BEGINNING WORK ON SUBSEQUENT PHASES.
- LOCAL DRIVEWAYS SHALL BE ACCESSIBLE AT ALL TIMES.
- AT LEAST ONE DRIVEWAY TO SAM'S CLUB SHALL REMAIN OPEN AT ALL TIMES.
- THE INTERSECTION OF US 67 AND SOUTHLAND BLVD SHALL REMAIN OPEN UNLESS APPROVED BY THE ENGINEER OR THE CITY OF SAN ANGELO.

PHASE 1 WIDENING OF SOUTHLAND BLVD.
- INSTALL BARRICADES AND TRAFFIC CONTROL DEVICES IN ADVANCE OF PHASE 1 CONSTRUCTION OR AS DIRECTED BY THE ENGINEER.
- INSTALL SW3P FOR PHASE 1
- PERFORM REMOVAL OF PORTIONS OF SOUTHLAND BLVD.
- PERFORM CULVERT EXTENSIONS.
- INSTALL TRAFFIC SIGNAL POLE.
- CONSTRUCT OUTSIDE WIDENING OF SOUTHLAND BLVD. AND SIDEWALK.

PHASE 2 MILL AND INLAY
- INSTALL BARRICADES, TRAFFIC CONTROL DEVICES, AND PORTABLE CHANGEABLE MESSAGE SIGN IN ADVANCE OF PHASE 2 CONSTRUCTION OR AS DIRECTED BY THE ENGINEER.
- INSTALL SW3P FOR PHASE 2
- MILL AND INLAY OF EXISTING PAVEMENT AREAS, OVERLAY OF WIDENED PAVEMENT AREAS AND MAINTAIN TRAFFIC AS A MOBILE OPERATION.
- PLACE FINAL PAVEMENT MARKINGS.

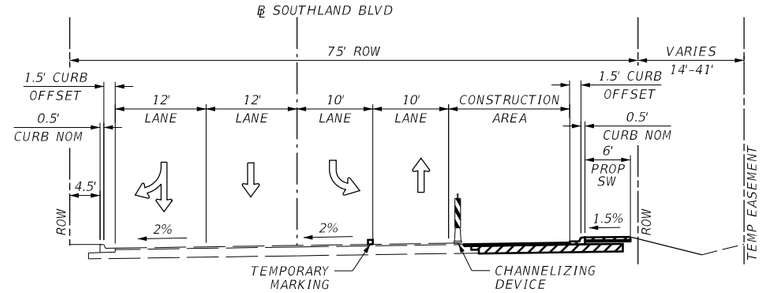

PHASE I SOUTHLAND BLVD

BEGIN TO STA 13+70

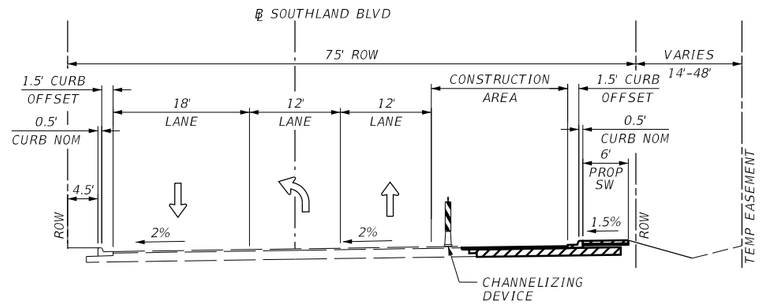

PHASE I SOUTHLAND BLVD

STA 13+70 TO END

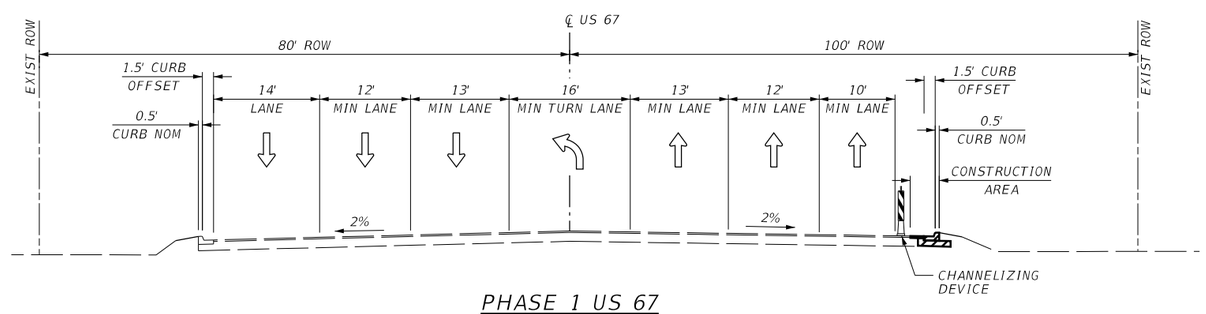

PHASE 1 US 67

US 67 AT SOUTHLAND BLVD

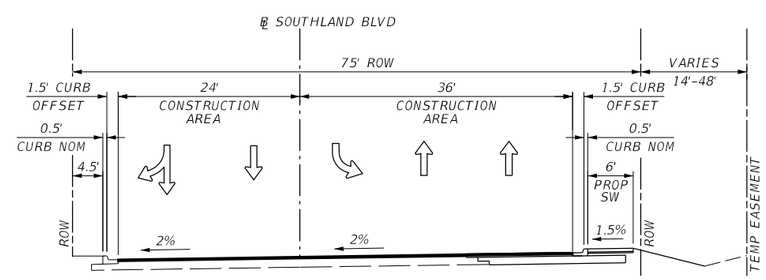

PHASE II SOUTHLAND BLVD

BEGIN TO END

LEGEND

PAVEMENT CONSTRUCTED THIS PHASE

NOTES:

1. A MINIMUM OF ONE THROUGH LANE EACH DIRECTION SHALL BE MAINTAINED ON SOUTHLAND BLVD. DURING ALL PHASES.
2. WORK DURING NIGHT TIME OR DURING LIMITED VISIBILITY IS PROHIBITED UNLESS DIRECTED BY THE ENGINEER.
3. DURING NON-WORKING HOURS, ALL DROP OFFS ARE TO BE FILLED OR PROTECTED. REFER TO WZ(UL)-13 AND TREATMENT FOR VARIOUS EDGE CONDITIONS AND DETAILS OR AS DIRECTED BY THE ENGINEER.
4. REFER TO TXDOT STANDARD SHEET TCP(2-1)-12 FOR WORK ZONE CHANNELIZATIONS AND SIGNAGE REQUIREMENTS OR AS DIRECTED BY THE ENGINEER.

09/23/2016

STATE OF TEXAS
MICHAEL C. COYLE
95634
LICENSED PROFESSIONAL ENGINEER

NOT TO SCALE

REV. NO.	DATE	DESCRIPTION	BY

LJA Engineering, Inc.
FRN-F-1386

THE CITY OF SAN ANGELO TEXAS

SOUTHLAND BOULEVARD
CONSTRUCTION SEQUENCE AND TYPICAL SECTIONS

SHEET 1 OF 1

SHEET NO. 7

11:07:19 AM 9/23/2016
T:\2357\1601\CADD\SHEETS\03-TCP\SB-TSC01-01.dgn
